

Autoflow Lifting Plan

Forklifting plan for Autoflow Mk4

Contents

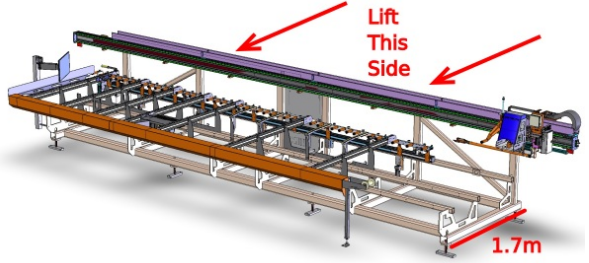
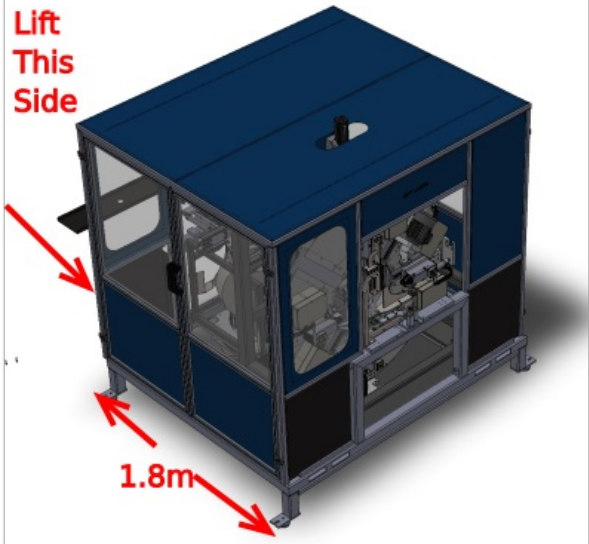
Forklift Requirements

Comments

Forklift Requirements

The Autoflow Mk4 is delivered in 3 main modules

Modules

	Name	Weight	Dims (l x w x h)	Notes	Pic
A	Infeed Table	2.5t	9.5m x 2.5m x 2m	<p>Very Important to lift from the side indicated</p> <p>Fork Extensions required to reach at least 300mm beyond 1.7m</p>	
B	Machining Module	2.0t	1.8m x 2.2m x 2.1m	<p>Very Important to lift from the side indicated</p> <p>Fork Extensions required to reach at least 300mm beyond 1.8m</p>	

C	Outfeed Table	0.5t	4.1m x 1.8m x1.2m	 <p>Lift This Side</p> <p>1.7m</p>
---	---------------	------	----------------------	---
